



EXECUTIVE SUMMARY REPORT

WAUNAKEE SCHOOLS: NEW INTERMEDIATE SCHOOL

Week ending January 15th, 2016

What's New?

Despite the cold temperatures, all precast panels were put in place this week. All of the topping for the precast was poured this week as well. Roofing is being placed on Area A & B and will continue as weather permits. Long span joists are being finished in the gym and the Area D mezzanine. Interior framing in Areas 2B & 1A is also going in this next week.

The Past Two Weeks

- Gym Joists and decking
- Precast panels put up around the gym
- Exterior framing and sheathing
- Interior framing
- Mechanical, Electrical, & Plumbing rough-ins
- Exterior glass framing

Coming Up in the Weeks Ahead

- Exterior stud framing Areas C & D
- Drywall installations in Area 2B
- Mechanical unit installations in Area D mezzanine



The last of the precast panels being installed at the Southeast corner of the gym.



Stairs in Area B were poured Tuesday and are functional for use.



Decking over choral and general music rooms in area C is currently being installed.



Did you know? The world record for the largest concrete pour in a single project is the Three Gorges Dam in Hubei Province, China by the Three Gorges Corporation. The amount of concrete used in the construction of the dam is estimated at 16 million cubic meters over 17 years.




EXECUTIVE SUMMARY REPORT

WAUNAKEE SCHOOLS: NEW INTERMEDIATE SCHOOL



Transferring supplies and equipment to the second floor with this reach forklift.

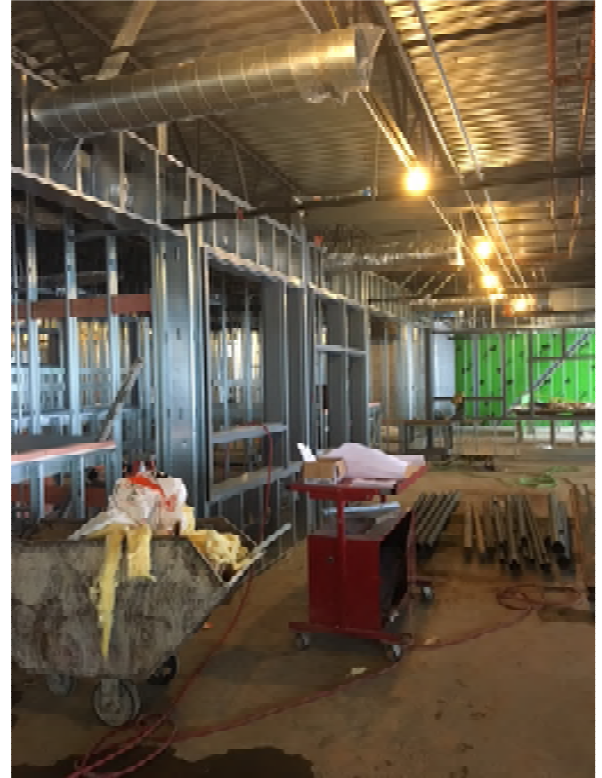

Area 2B is ready for drywall!



Aerial shot of the jobsite looking north
