



EXECUTIVE SUMMARY REPORT

WAUNAKEE SCHOOLS: NEW INTERMEDIATE SCHOOL

Week ending May 20th, 2016

What's New?

Over the past few weeks, sitework has ramped up in many areas across the job site. The final seeding on the South Playing Field have been planted. Final grading and concrete preparation for parking areas started last week as well. On the interior, resilient flooring is being set on second floor Area B corridor, toilet partitions are being put in on second floor, and food service equipment was installed in the kitchen. In addition, drywall soffits are going in everywhere to hide MEP activity.

The Past Two Weeks

- Doors and Hardware install – 2nd floor & section 1A
- Exterior Metal Panels
- Site grading and driveway prep
- Resilient Flooring in corridors - 2nd floor
- Elevator Install

Coming Up in the Weeks Ahead

- Wood flooring, striping & sealing - Gym
- Ceiling tile in area 2B
- Testing and inspections – 2nd floor
- Curb and gutter install
- Punchlists and walkthroughs – section 2B



The equipment shed is built and the sidewalk near the lacrosse field is ready for concrete.



A full four-door fridge/freezer was recently installed in the kitchen



Take a look at the new redwood metal panels. They will cover the west elevation (above) along with all the recessed areas around the exterior of the building (left).



Did you know? Although elevators may seem like a modern invention, Greek mathematician Archimedes created the first primitive elevator in 236 B.C. It was operated by hoisting ropes wound around a drum and rotated by manpower applied to a capstan.



EXECUTIVE SUMMARY REPORT

WAUNAKEE SCHOOLS: NEW INTERMEDIATE SCHOOL



With the installation of toilet partitions, the bathrooms on the second floor are nearly complete (above).

Area 2B is currently blocked off to everyone to allow the resilient flooring tile to set (below).




The touchstone and mission statements were relocated from the existing Intermediate School the new gym last week (above).

The ceiling finish above the social stairs is definitely going to have a "wow" factor (left).



The touchstone and mission statements were relocated from the existing Intermediate School the new gym last week (above).

The ceiling finish above the social stairs is definitely going to have a "wow" factor (left).

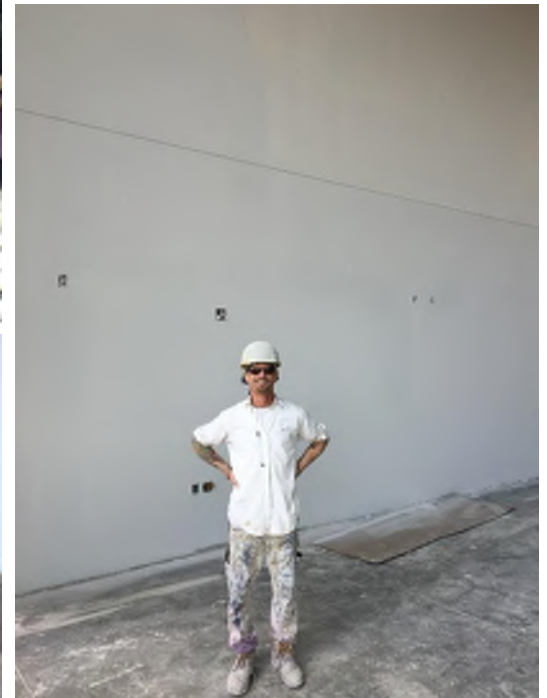

A satisfied painter in front of his work after a long day.
