



EXECUTIVE SUMMARY REPORT

WAUNAKEE SCHOOLS: PRAIRIE ELEMENTARY

Week ending July 17, 2015

What's New?

The addition became watertight and drywall was installed throughout along with some hollow metal frames. Continued work on the addition in the coming weeks include painting block, taping, and painting. In the existing building, most demo is coming to a close with new drywall, flooring, electrical work to be installed within the new couple weeks.

The Past Week

- Addition watertight
- Drywall installed in addition
- Some hollow metal door frames installed
- Sanitary sewer/water line installation
- Gym lighting and new curtain hung

Coming Up in the Week Ahead

- Painting of block and drywall
- Acoustical grid ceiling and MEP trim
- Gym floor installation
- Fire Alarm and other low voltage work ongoing



Demolition completed in this classroom, and materials for the renovation are waiting for workers to install.



One of the new playground locations for the K-2 side.



The gym curtain right before it was hung in the gym!




Did you know? In Ethiopia, kids have summer vacation for 3-4 months, rather than kids in the United States only having summer vacation for only 2.5-3 months.



EXECUTIVE SUMMARY REPORT

WAUNAKEE SCHOOLS: PRAIRIE ELEMENTARY

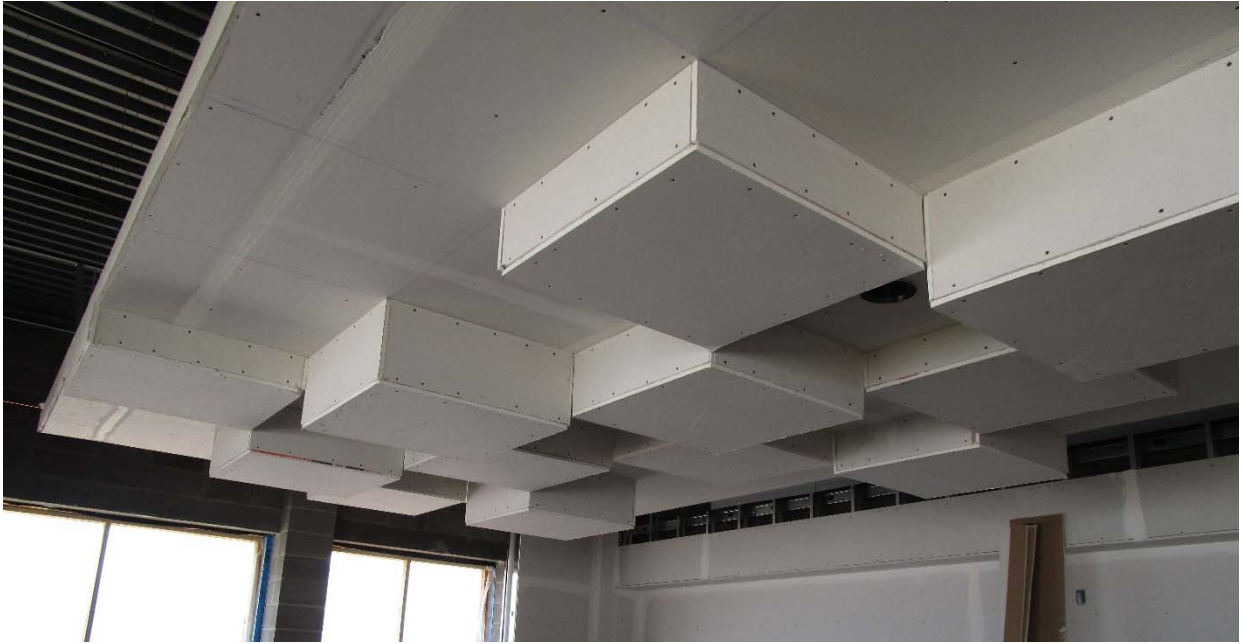

New three-dimensional ceiling in the breakout area.



New column bump outs to receive new sections of storage cubbies. This is located in the existing building.



A classroom that has undergone demolition, and will see new flooring.
