



EXECUTIVE SUMMARY REPORT

WAUNAKEE SCHOOLS: NEW INTERMEDIATE SCHOOL

Week ending December 18th, 2015

What's New?

The gym joists were completed last week, and steel decking installation began in the LMTC area. Area B exterior studs and dens glass were completed with a layer of weather barrier applied, and Area A now has most studs and dens glass installed as well. The ductwork in Area 2B is almost complete, and started in Area 1A this week, with other MEPs continuing work in Area A and B.

The Past Two Weeks

- Gym Joists
- Exterior framing and sheathing
- Continued interior masonry in Areas A, C, & D
- Steel decking in gymnasium and LMTC

Coming Up in the Weeks Ahead

- Roofing in Area B and A
- Continued steel stud wall framing and dens glass sheathing
- Continued decking and detailing in Area A
- Continued MEP Rough-ins



Dens glass with a layer of weather barrier applied. Temporary window enclosures installed on the windows.



Masons working on the Area D restroom.



Steel decking installation in the library area.



Did you know? CMU block is one of the best construction materials because it is strong, mold resistant, and very slow to absorb/lose heat. One 8" CMU block can support 205 Sumo Wrestlers if they weigh 500 lbs. on average. That is over 100,000 lbs!




EXECUTIVE SUMMARY REPORT

WAUNAKEE SCHOOLS: NEW INTERMEDIATE SCHOOL



Most of the ductwork in Area B has been completed as shown, and they have moved to the first floor.

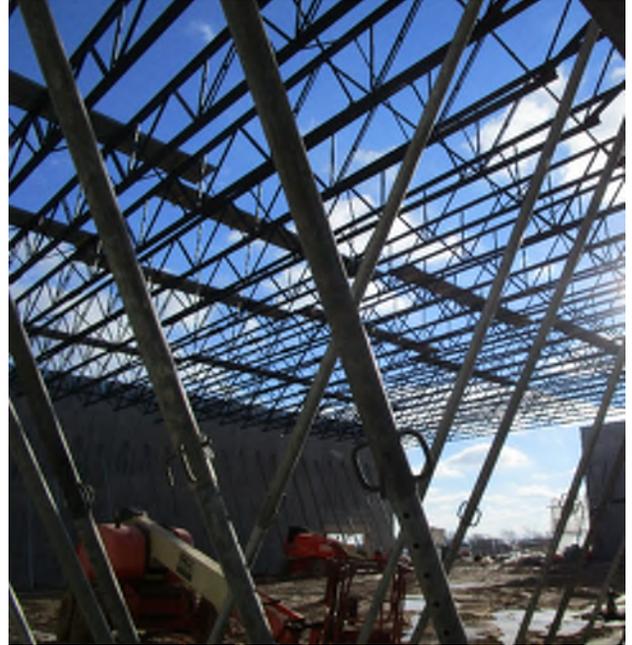

The large gym joists were installed last week in just 3 days!



Progress of the overall school with all exterior studs and dens glass in B completed with a layer of waterproofing completed. Area A has most exterior studs up also, with dens glass going up there as well.
